



Environmental Monitoring Summary Report Port Kembla Gas Terminal

Infrastructure ApprovalSSI-9471EPL Licence Number:21529

Reporting period:1 January 2023 – 31 January 2023

Date published:

23 February 2023



1 Project background

AIE is responsible for the development of a liquefied natural gas (LNG) import terminal at Port Kembla, south of Wollongong, NSW (the Project). The Project will be the first of its kind in NSW and will provide a simple and flexible solution to the state's gas supply challenges.

The Project has been declared Critical State Significant Infrastructure (CSSI) in accordance with Section 5.13 of the *Environmental Planning and Assessment Act 1979* (EP&A Act) (NSW) and Schedule 5 of the *State Environmental Planning Policy State and Regional Development* (SRD SEPP). The Project received Infrastructure Approval from the Minister for Planning and Public Spaces on 29 of April 2019.

The construction of the Project is primarily associated with the establishment of a new berth facility at Port Kembla to enable a Liquified Natural Gas (LNG) Carrier to berth alongside the Floating Storage and Regasification Unit (FSRU) and new infrastructure to connect the terminal to the existing gas network. The location of the Project is shown on the Environmental Monitoring Location Plan provided as Appendix A.

An Environment Protection Licence (EPL) (EPL No. 21529) was issued for the Project by the NSW Environment Protection Authority (EPA) on 2 June 2021. The details of the EPL are provided below in Table 1-1.

EPL No.	21529					
Anniversary Date:	2 June					
	Australian Industrial Energy Pty Ltd					
Licensee:	PO Box 3155 Broadway					
	Nedlands WA 6009					
Premises:	Port Kembla Gas Terminal, Port Kembla NSW 2505					
	Contaminated soil treatment					
Scheduled Activity	Crushing, grinding or separating					
	Petroleum products storage					

Table 1-1 EPL Details



2 Report purpose

This Monthly Environmental Monitoring Report has been prepared to provide an overview of project activities undertaken during the reporting period and those forecast for the next reporting period (refer to Section 3), and to satisfy the requirements associated with the reporting and publishing of monitoring data and results required under the relevant conditions of approval and environmental management plans as detailed further in Table 2-1.

Document	Clause or section	Requirement	Addressed:		
	Sch. 4 Cond. 8	Regular Reporting – The Proponent must provide regular reporting on the environmental performance of the development on its website in accordance with the reporting requirements in any strategies, plans or programs approved under the conditions of this approval.	This report which will be made available on		
DPIE SSI-9471		 Access to information – From the commencement of development under this approval, the Proponent shall: (a) Make copies of the following information publicly available on its website: 	the Project Website.		
	Sch. 4 Cond. 12	 a comprehensive summary of the monitoring results of the development, reported in accordance with the specifications in any conditions of this approval, or any approved plans and programs 	Section 4		
		- a summary of complaints, which is to be updated monthly	Section 5		
AIE Air Quality Management Plan (Stage 2A and 2B)	Section 11.4	A monthly environmental monitoring report will be developed for each calendar month which will include details of the monitoring results and frequencies and inclusion of any exceedance of EPL No. 21529 air monitoring limits / criteria. A copy of the monthly environmental monitoring report will be made available on the AIE Project website.	Air quality monitoring results and frequencies and inclusion of any exceedance provided in Section 4.1		
AIE Water Quality Monitoring Plan (Stage 2A and 2B)	Section 9.4	A monthly environmental monitoring report will be developed for each calendar month which will include details of the monitoring results and frequencies and inclusion of any exceedance of EPL (No. 21529) water quality monitoring limits / criteria. A copy of the monthly environmental monitoring report will be made available on the AIE Project website.	Water quality monitoring results and frequencies and inclusion of any exceedance provided in Section 4.2		
EPL 21529	Condition M6.2	The licensee must monitor and record temperature, humidity, wind direction, wind velocity and rainfall at either the project weather station, or through analysis of equivalent weather information obtained from the Australian Bureau of Meteorology. Whilst there are no specific requirements to provide weather data in the monthly report, AIE has included the data for transparency and to assist with context for any monitoring results where required.	Section 4.3		



3 Project activities

3.1 Project status

The project has progressed to Stage 2A and Stage 2B as follows:

Stage 2A: Marine Berth Construction – Land Based. Associated works include:

- Quay wall construction.
- Installation of communications conduit, potable water line, and 11kV power cable and Pad-mount Substation within the Marine Berth Construction and Dredging (MBD) Site Compound.
- Construction of the Onshore Receiving Facilities (ORF), which comprises three areas: Wharf Topside Area; Utility Area; and Common Area.
- Pipeline construction and associated ancillary infrastructure within MBD Site Compound delivered as part of ORF scope.

Stage 2B: Marine Berth Construction – Marine Based. Associated works include:

- Continuation of Stage 2A works
- Excavation and dredging of the MBD Site Compound in the Inner Harbour and the Emplacement Cell in the Outer Harbour.
- Construction of the Emplacement Cell in the Outer Harbour.
- Marine based construction activities including installation of navigational aids and revetments at the MBD Site Compound.

Stage 3: Gas pipeline Construction. Associated works include:

- Construction of gas pipeline section within Berth 101.
- 3.2 Project activities for the reporting month
 - Continued dredging of Berth 101 and relocation of dredge spoil to the OH.
 - Construction of the Outer Harbour Emplacement Cell.
- 3.3 Project activities for the upcoming month
 - Ongoing dredging at Berth 101.
 - Construction of the Outer Harbour Emplacement Cell.



4 Environmental monitoring data

The following sections present a summary of the air quality, water quality and weather monitoring data for the reporting month.

A copy of this report will be made available on the Project website at the following web-address:

https://ausindenergy.com/environmental-information/

4.1 Air quality

4.1.1 Air Quality Monitoring Locations and Frequency

Air quality monitoring equipment is installed to the north and south of the MBD site compound (Berth 101), and to the east, to the west, and within the central portion of the Outer Harbour stockpile area.

A summary of the air quality monitoring locations is provided below in Table 4-1 and a monitoring location plan is provided in **Appendix A**.

Table 4-1 Air quality monitoring locations

EPL Ref.	Monitoring location	Monitoring type	Monitoring parameter	Monitoring frequency		
8	Northern boundary of the premises, adjacent the southern boundary of Port Kembla Coal Terminal	Dust Deposition	Particulates -	Monthly		
10	Southern boundary of Berth 101	Gauge	Deposited Matter (gm/m²/month)	Wontiny		
12	Southern side of emplacement area, Outer Harbour	Ambient Air Monitoring -	Total suspended	Special Frequency 1		
14	Eastern side of emplacement area, Outer Harbour	High Volume Air Sampler	particles (TSP) (ug/m ³)	(24-hour period every 6 days)		
22	Northern side of emplacement area, Outer Harbour					
9	Northern boundary of the premises, adjacent the southern boundary of Port Kembla Coal Terminal					
11	Southern boundary of Berth 101					
13	Southern side of emplacement area, Outer Harbour	Real time dust monitoring	PM10 (ug/m³)	Continuous		
15	Eastern side of emplacement area, Outer Harbour					
23	Northern side of emplacement area, Outer Harbour					



4.1.2 Air Quality Monitoring Results

The air quality monitoring results for the reporting month are presented below in Table 4-2.

Tabla	1 2 Air	avality	monitoring	roculto
rubie	4-2 All	quanty	monitoring	resuits

					Monitoring	parameter			
			Total Su	spended Pa	rticulate				
		Particulates	(High V	olume Air Sa	ampler)	(Real-time			
Monitoring Location (EPL Reference)		Deposited Matter (Depositional dust gauge)**	Average	Min.	Max.	Average	Min.	Max.	Events above criteria*
Unit		g/m²/month	mg/m ³	mg/m ³	mg/m ³	ug/m³/24 hr average	No.		
Criteria		NA	NA	NA	NA	NA	NA	200	NA
Berth 101	EPL 8	5.00	0.09	0.07	0.10	No PM10 n tł	•		
North	EPL 9	No Dust Depo	sition Gaug at this EPL	•	required	47.55	18.13	90.88	0
Berth 101	EPL 10	3.60	0.08	0.04	0.10	No PM10 n tł			
South	EPL 11	No Dust Depo	sition Gaug at this EPL	•	required	32.06	19.54	49.83	0
Outer	EPL 12	1.50	0.04	0.02	0.05		nonitoring r nis EPL Poin	•	
Harbour South	EPL 13	No Dust Depo	sition Gaug at this EPL	•	required	23.62	9.51	44.83	0
Outer	EPL 14	0.70	0.05	0.03	0.06		nonitoring r nis EPL Poin	•	
Harbour East	EPL 15	No Dust Depo	sition Gaug at this EPL	•	required	21.04	7.77	37.49	0
Outer Harbour	EPL 22	1.20	0.04	0.03	0.05	No PM10 n tł	nonitoring r nis EPL Poin	•	
North	EPL 23	 No Dust Deposition Gauge or HiVol required at this EPL Point 				16.66	5.96	49.10	0

*Includes individual number of times results recorded above Stage 2A and Stage 2B performance criteria (200 ug/m³/24 hour average). Refer to **Appendix B** for event above criteria reports.

**Assessed as Total Insoluble.



4.2 Water quality

4.2.1 Water Quality Monitoring Locations and Frequency

Water quality monitoring is undertaken at five (5) locations within the Port Kembla Harbour. Each water quality monitoring location is securely anchored/moored in its location. Details of each of the water quality monitoring locations and corresponding EPL monitoring point reference is provided below in Table 4-3.

Table 4-3 Port Kembla Harbour water quality monitoring loco	
- TUDIE 4-3 FUTE KETTIDIA TIAIDUAT WALET AAAIILV TITUTILUTITA TULE	tions

EPL			Parameters				
Ref.	Monitoring location	Type of monitoring	Continuous monitoring at 15 min intervals	Weekly grab sample			
1	WQM1 - North of Berth 101	Primary- impact works area receiver		- Aluminium - Arsenic			
16	WQM2 - North of the emplacement cell, Outer Harbour.	Primary- impact works area receiver	- Turbidity	 Cadmium Chromium (total) Cobalt 			
17	WQM3 - South West of Berth 101	Primary- impact works area receiver	- Temperature - pH	- Copper - Lead			
18	WQM4 - Near the Pacific Ocean entrance to Outer Harbour	Background water quality	 Salinity (EC) Dissolved oxygen 	- Mercury - Nickel - Total PAHs - TSS			
19	WQM5 - Near entrance to Allans Creek, near BlueScope Steel	Background water quality		- Tributyltin - Zinc			

It is noted that the EPL 21529 also includes a mobile water quality monitoring point (EPL 24) for the undertaking of ambient water quality monitoring for turbidity within 5m of the outermost silt curtain near Berth 101 during dredging operations. As dredging works at Berth 101 continued throughout this reporting period, water quality monitoring was in place at EPL 24.

In addition to the monitoring requirements listed above for the harbour, monitoring is also required for any discharge event from the on-site sedimentation basin located at the southern end of Berth 101. Details of the monitoring requirements associated with the sediment basin discharge point are included below in Table 4-4.

Table 4-4 Sediment basin discharge monitoring

EPL	Monitoring location	Type of monitoring	Parameters						
Ref.	f. Fight and the second s	Type of monitoring	Prior to discharge	Daily grab sample	e during discharge				
20	Sediment basin discharge point at the southern end of Berth 101	Wet weather discharge quality	 Oil and grease (visual) Total suspended solids (TSS) 	 Aluminium Arsenic Cadmium Chromium Cobalt Copper Lead Mercury 	 Nickel Oil and grease (visual) pH Total PAHs Tributyltin TSS Zinc 				



4.2.2 Water Quality Monitoring Results

A summary of the results for the continuous water quality monitoring in Port Kembla Harbour is presented below in Table 4-5. Further details for exceedances as indicated below (if applicable) are provided in **Appendix B**.

			Results - based	d on individual 1	5-minute media	n
	Statistic	Turbidity (NTU)	Temperature (Deg. C)	Hd	Electrical conductivity (uS/cm2)	Dissolved Oxygen (%sat)
Criteria		50 + BG ¹	N/A	6.5 – 8.5	N/A	70 - 110
	Average	3.8	23.2	8.2	52375.2	99.1
WQM1	Minimum	1.6	20.6	8.1	41745.7	81.9
EPL 1	Maximum	1133.2	26.6	8.4	53756.0	132.8
	Events above criteria ²	3	-	0	-	14
	Average	3.5	23.0	8.2	53171.6	114.7
WQM2 EPL 16	Minimum	0.0	20.4	8.2	52050.3	94.8
	Maximum	915.0	27.8	8.4	53567.1	141.1
	Events above criteria ²	5	-	0	-	29
	Average	2.7	23.3	8.3	52787.2	103.2
WQM3	Minimum	1.4	20.6	8.0	47378.9	83.3
EPL 17	Maximum	29.6	28.5	8.5	53711.2	142.2
	Events above criteria ²	0	-	0	-	21
WQM4	Average	3.6	22.7	8.3	52927.3	102.9
EPL 18	Minimum	0.0	20.4	7.9	33575.8	84.2
(Background)	Maximum	987.3	27.3	8.4	53563.6	136.5
WQM5	Average	3.9	27.4	8.3	51422.5	103.4
EPL 19	Minimum	1.2	22.1	8.1	31956.5	89.8
(Background)	Maximum	53.5	32.0	8.5	53795.2	122.6
Mobile WQM /	Average	1.76				
EPL 24	Minimum	0.19		Not required	at this EPL Point	
(Ambient) ³	Maximum	10.04				

Table 4-5 Port Kembla Harbour water quality – Continuous monitoring results

¹Total suspended solids (TSS) is monitored in real time using turbidity in NTU and the NTU-TSS correlation as recommended in the current EPL or from an in-field study approved by the EPA, whichever is more current at the time of measurement. BG = Background, recorded at WQM4 and/or WQM5.

²Calculated as number of days where results exceeded performance criteria. Refer to Appendix B for exceedance reports.

³Complete results for this point are included as Appendix C.



4.2.3 Water Quality Monitoring Results – Port Kembla Harbour Grab Samples

A summary of the results for the Port Kembla Harbour weekly grab samples is presented below in Table 4-6. Further details for exceedances as indicated below (if applicable) are provided in **Appendix B**.

Table 4-6 Port Kembla Harbour water quality – Weekly grab sample results summary

Monitoring Location	Statistic ²	Aluminium	Arsenic	Cadmium	Chromium (total)	Cobalt	Copper	Lead	Mercury	Nickel	Total PAHs	Total Suspended Solids (TSS)	Tributyltin	Zinc
Unit		ug/L	ug/L	ug/L	ug/L	ug/L	ug/L	ug/L	Ug/L	ug/L	ug/L	mg/L	ngSn/L	ug/L
Criteria		200	50	5.5	4.4	1	8	12	0.4	70	50	50	6	21
	Average	<5	1.67	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
WQM1	Minimum	<5	1.60	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
EPL 1	Maximum	<5	1.70	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
	Events above criteria ¹	0	0	0	0	0	0	0	0	0	0	0	0	0
	Average	<5	1.63	<1	<0.5	<1	1.00	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
WQM2	Minimum	<5	1.50	<1	<0.5	<1	1.00	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
EPL 16	Maximum	<5	1.80	<1	<0.5	<1	1.00	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
	Events above criteria ¹	0	0	0	0	0	0	0	0	0	0	0	0	0
	Average	<5	1.60	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
WQM3	Minimum	<5	1.60	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
EPL 17	Maximum	<5	1.60	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
	Events above criteria ¹	0	0	0	0	0	0	0	0	0	0	0	0	0
WQM4	Average	<5	1.70	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
EPL 18	Minimum	<5	1.50	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
	Maximum	<5	1.90	<1	<0.5	<1	<1	<0.2	<0.1	<0.5	<0.05	<5	<2	<5
	Average	<5	1.90	<1	<0.5	<1	1.00	<0.2	<0.1	5.00	<0.05	<5	<2	9.00
WQM5	Minimum	<5	1.60	<1	<0.5	<1	1.00	<0.2	<0.1	5.00	<0.05	<5	<2	9.00
EPL 19	Maximum	<5	2.40	<1	<0.5	<1	1.00	<0.2	<0.1	5.00	<0.05	<5	<2	9.00

¹Includes individual number of times results exceeded criteria. Refer to **Appendix B** for exceedance reports.

²Only results above the laboratory Limit of Reporting (LOR) have been used to calculate these data functions. Where an analyte has not been detected above the LOR throughout the monitoring period, the LOR has been listed.



4.2.4 Water Quality Monitoring Results – Sediment basin discharge

During the reporting month, there were two (2) authorised discharge events, and zero (0) discharge events as a result of excessive rainfall exceeding the design criteria of the basin (>43.5 mm in any 5-day period). Refer to Section 4.3 for site weather monitoring details. The date of the events and a summary of the water quality results for the authorised discharge events from the sediment basin is included below in Table 4-7.

Date of discharge/ sampling	Aluminium	Arsenic	Cadmium	Chromium	Cobalt	Copper	Lead	Mercury	Nickel	Zinc	Tributyltin	TSS	Hq	Oil & Grease	Total PAH	Overflow Discharge?	Rainfall (mm) Roll. 5-Day Total
	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	μg/L	mg/L	-	-	μg/L	-	mm
Criteria	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	50	NA	Visible	NA	NA	NA
27/01/2023	544.00	1.40	0.08	0.40	<0.1	2.20	<0.1	<0.1	<0.5	8.00	<2	8.00	8.68	<5	<0.05	Ν	NA
30/01/2023	591.00	1.40	0.08	0.40	<0.1	2.20	<0.1	<0.1	<0.5	8.00	<2	8.00	8.68	<5	<0.05	Ν	NA

Table 4-7 Sediment basin discharge water quality – Pre-discharge and daily grab sample results



4.3 Weather station results

Under the EPL (Condition M6.2), AIE is required to monitor and record temperature, humidity, wind direction, wind velocity and rainfall at either a project weather station, or through analysis of equivalent weather information obtained from the Australian Bureau of Meteorology.

AlE established and maintains a weather station for the project site located at the southern point of Berth 101 (EPL monitoring point 21) as shown in **Appendix A**. The data obtained from the onsite weather station for the reporting period is provided below in Table 4-8.

Parameter	Unit of measure	Monthly statistic	Result EPL 21
	m/s	Average	4.37
Wind velocity	(15min average)	Minimum	0.17
		Maximum	11.13
Wind direction at 10m	Degrees 1 hour averaging period)	See Wind Rose cl	nart (Figure 4-1)
	mm/hr	Average	0.01
Rainfall rate	(1 hour averaging period)	Minimum	0.00
		Maximum	1.15
	mm/day	Average	2.81
Rainfall (Total)		Minimum	0.00
		Maximum	30.80
		Average	21.64
Temperature	Degrees Celsius	Minimum	15.00
		Maximum	27.30
		Average	80.08
Humidity	%	Minimum	53.20
		Maximum	100.00

Table 4-8 Site weather station monitoring results summary



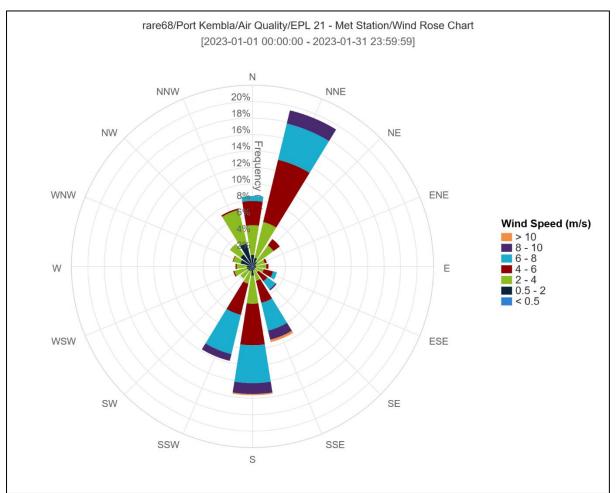


Figure 4-1 Wind Rose chart for the reporting period.



5 Environmental complaints

A summary of environmental complaints received during the reporting month and follow-up, close-out and or corrective actions are presented below in Table 5-1 where applicable.

Table 5-1 Environmental complaints summary


Date	Complaint No.	Nature of the complaint	Follow-up close-out and or corrective action
25/01/2023	05	Complaint received by the NSW EPA on 18/01/2023 and passed on to AIE 25/01/2023. Dust complaint from a business in the vicinity of your operations in the Outer Harbour / Foreshore Road area.	Detailed investigation undertaken by AIE, including review of weather conditions and review of work activities being undertaken at the time of the complaint. The investigation determined that the source of the dust was not related to AIE activities. This was communicated back to the EPA in a letter dated 01/02/2023. AIE to continue undertaking air quality monitoring and implementing dust mitigation measures as per the AIE Stage 2A and 2B Air Quality Management Plan.



Appendices

Page 14 of 14

Appendix A - Monitoring Location Plan

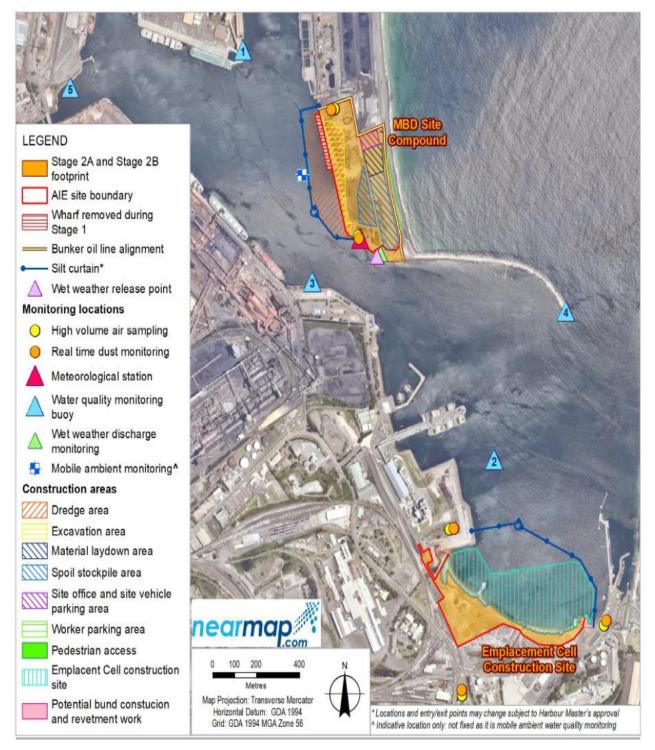


Appendix B – Summary of Events Above Criteria

Each exceedance triggers an investigation including the nature of project activities being undertaken, evaluation of wind direction, comparison of upwind and downwind monitors at the time of the event. Dust prevention controls are continually being assessed to ensure their adequacy.

Air Monitoring Events Above Criteria

Date	Location	Exceedance value (ug/m ³ /24 hours)	Action Taken & Investigation Outcomes
-	-	-	No exceedances in January 2023

Water Monitoring Events Above Criteria: Harbour water quality - Continuous monitoring results

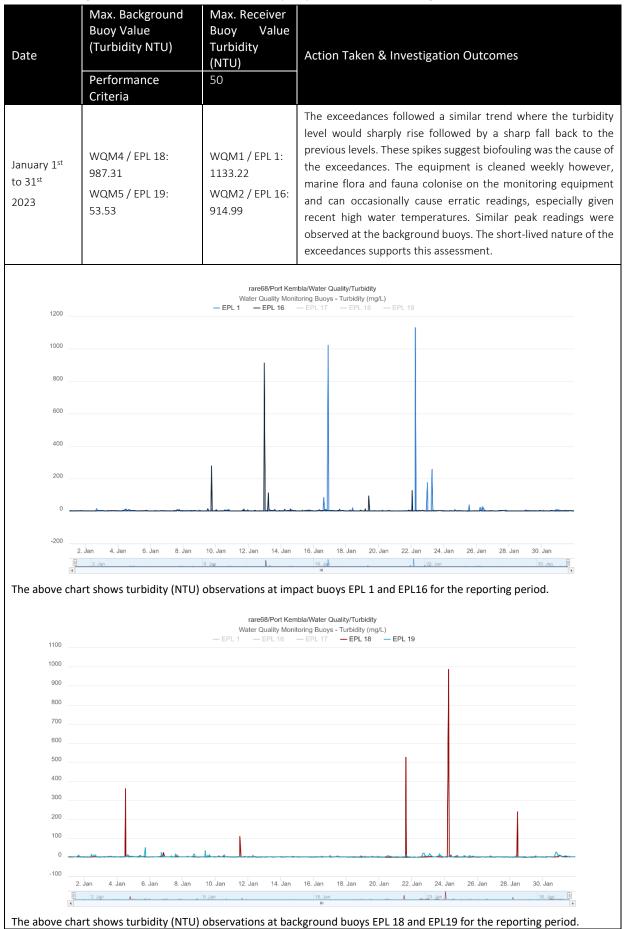

Date	Max. Background Buoy Value (DO%) Performance Criteria	Max. Receiver Buoy Value (DO%) 70 – 110	Action Taken & Investigation Outcomes
January 1 st to 31 st 2023	WQM4 / EPL 18: 143.75 WQM5 / EPL 19: 125.36	WQM1 / EPL 1: 156.89 WQM2 / EPL 16: 147.86 WQM3 / EPL 17: 169.33	Dissolved Oxygen (DO) is a measure of the amount of oxygen available to living aquatic organisms. The project has adopted performance criteria as described by the <i>National Acid Sulfate</i> <i>Soils Guidance (NAASG)</i> for the monitoring of DO during dredging activities. Dredging of acid sulfate soils can result in the reduction of dissolved oxygen in a waterbody due to pyrite (a key component of acid sulfate soils) combining with oxygen to create sulfate compounds such as sulfuric acid. The <i>NAASG</i> suggests a performance criterion for DO of greater than 50% saturation for this reason. These exceedances of the performance criteria were an excess of DO saturation, not a reduction. The high DO levels observed in the harbour are related to several external factors to the project including atmospheric pressure and water temperature, tidal cycles and wind.
rare68/Port Kembla/Water Quality/Dissolved Oxygen Water Quality Monitoring Buoys - Dissolved Oxygen (%) — EPL 1 — EPL 16 — EPL 17 — EPL 18 — EPL 19			
140 130 120 110	M Martin Auto	MAAAAA	Manhaman

90 70 2. Jan 4. Jan 6. Jan 8. Jan 10. Jan 12. Jan 14. Jan 16. Jan 18. Jan 20. Jan 22. Jan 24. Jan 28. Jan 30. Jan The above chart shows DO observations at impact buoys EPL 1, EPL16 and EPL 17, as well as at background buoys; EPL 18 and EPL 19 for the reporting period.

Appendix C – EPL 24 Data

This is a mobile monitoring point located five metres outside the silt curtain around Berth 101. Point 24 is required to be sampled daily for Total Suspended Solids (TSS) during dredging activities. TSS is monitored in real time using turbidity in NTU and the NTU-TSS correlation as recommended in the current EPL or from an in-field study approved by the EPA, whichever is more current at the time of measurement.

EPL 24 Daily Average Monitoring Results		
Date	Turbidity (NTU)	
1/01/2023	-	
2/01/2023	-	
3/01/2023	-	
4/01/2023	1.55	
5/01/2023	0.73	
6/01/2023	1.47	
7/01/2023	1.62	
8/01/2023	3.25	
9/01/2023	1.31	
10/01/2023	1.85	
11/01/2023	1.57	
12/01/2023	1.49	
13/01/2023	3.18	
14/01/2023	1.31	
15/01/2023	1.50	
16/01/2023	1.61	
17/01/2023	2.01	
18/01/2023	1.70	
19/01/2023	1.48	
20/01/2023	1.11	
21/01/2023	0.58	
22/01/2023	2.31	
23/01/2023	1.19	
24/01/2023	1.17	
25/01/2023	1.79	
26/01/2023	1.12	
27/01/2023	1.80	
28/01/2023	1.40	
29/01/2023	1.00	
30/01/2023	2.10	
31/01/2023	2.88	
Note: For dates where no results are recorded, no dredging activitie		

Note: For dates where no results are recorded, no dredging activities at Berth 101 were undertaken.
